
Completion Report

Homelands Housing and Infrastructure Program





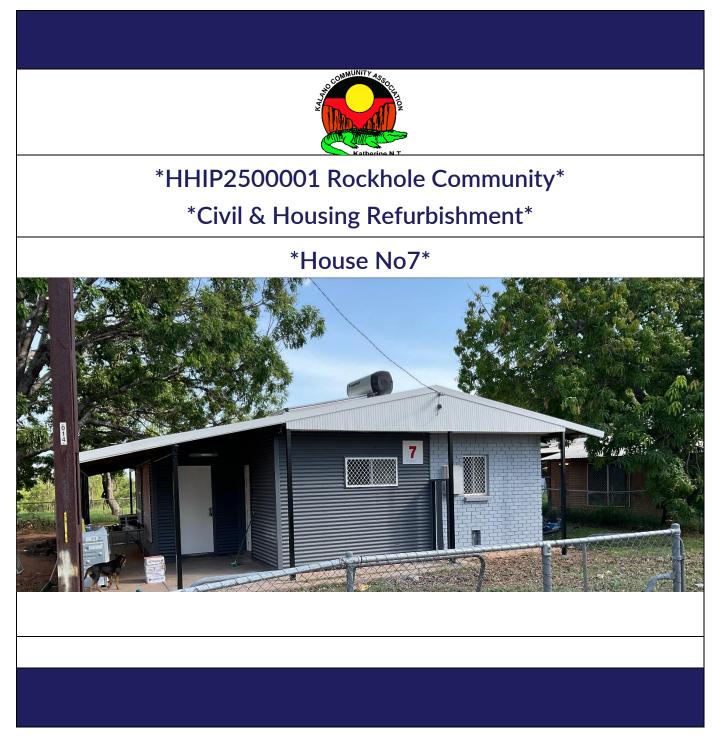

Contents

Project Summary	
Scope of Works Overview	
Visual Progress	
Attachments	
Final Review and Acceptance	Error! Bookmark not defined.

Service Provider	Kalano Community Association	ABN	17 030 032 930
Contact Details	Alan Mole (CEO) <u>ceo@kalano.org.au</u> Nashe Kasiyan (Project Manager) nkasiyan@kalano.org.au	Contractor Accreditation Limited (CAL) Registration Number:	К-3-1451-09-25
Project Name	Rockhole Refurbishment	Contract No.	HHIP2500001
Homeland	Rockhole Community	Community ID	642
Project Type	Housing upgrades	House #	7
Commencement Date	22/12/2024	Completion Date	08/01/2024 (delay due to extension works)

Project Summary

Community Association have completed the housing upgrade works to House 7 in Rockhole on behalf of the NT Government's Homelands Housing Infrastructure Program (HHIP).

The works were completed in line with the Scope of Works listed in this report. Kalano made provisions of temporary accommodation for resident, scoping of works to upgrade home to current living standards under the latest building code guidelines for electrical, ventilation, accessibility & sanitation. The aim was to ensure the home & the community met the 9 Healthy Living Principles in the NT. Kalano also organised safe & lockable container storage facility for residents while works were underway. Residents were encouraged to choose the colour of finishes they wanted in their homes during scoping consultations and any special requirements that would enhance their living experience in the home.

Menzie's Health also ran a study on works being carried out in the upgrades not just for House 7 but for all. Works to the community upgrades contributed to the Chief Ministers' Awards nomination win in 2024 for the HHIP Team



Scope of Works Overview

Homeland: Rockhole Community, Florina Road, Katherine		
House/Asset No:	House 7	
Scoping Date:	15/07/2023	
Throughout the Dwelling		
Required Maintenance Works		
Environmental Clean		
• Repaint all internal walls, cei	iling, door, door frames and window frames.	
Repaint external walls and re	pof.	
• Multiple lights (internal and	external) not working – inspect and repair.	
Inspect Fire Alarms and insta	all where missing.	
Install night latch on all door	'S.	
• Install curtain hooks in all wi	ndows.	
Install Crim safe to all windo	ws and door flyscreen to match where missing.	
Exterior		
Tighten existing clothes line	and add extra lines where missing.	
	front of the house unless other suitable options available.	
Lounge/Kitchen		
Flyscreen is bent and off the	e window - needs replacement to Crim safe.	
• No electrical supply, inspect	and repair.	
• Replace light – missing bulb	and cover.	
• Flooring requires cleaning.		
 Inspect smoke alarm and rep 	pair/replace as required.	
• No air conditioning unit in th	nis room – install.	
Kitchen		
• Reinstate fly screen.		
Replace kitchen shelves with	n stainless steel shelves.	
• Cooktop /Oven - doesn't w	ork – only two hot plates are operational – Replace.	
Replace existing damaged fl	ooring with tiles.	



Bathroom

Toilet

- Replace tiles stained and rusty.
- Leaking water inspect for any plumbing issues and repair.
- Replace Toilet bowl.

Shower

- Shower head, shower taps, and sink taps to be removed and replace with quarter turn hand levers.
- Replace tiles stained and rusty.

Laundry

- Fix wall panel for the cupboard.
- Change taps to levers.

Bedroom 1

- Reinstate fly screen.
- Reinstate fan to the ceiling, hanging loose.
- No air conditioning unit in this room install.
- Install night latch on door.

Bedroom 2

- Reinstate fly screen.
- Door handle missing reinstate; install night latch.
- Reattach fan switch to the wall.
- Replace air conditioning unit.




Bedroom 3 (New)

- Pest control and certificate
- Concrete footings. For homes on the ground concrete slab
- Galvanised steel wall frames and trusses
- Roof and ceiling batons zincalume (steel)
- Color bond fabricated fascia
- Color bond corrugated roofing
- Cyclone roof assembly screws
- Cyclone ridge assembly fixed to ridge cap.
- 8mm etherm insulations over roof area
- Powder coated black alum expanded mesh vermin proofing.
- Color bond corrugated wall cladding, screw fixed.
- Wall framing insulated with 8mm etherm.
- External wall frames insulated internally with fiberglass bats (R1.5)
- Steel door frames with 920mm wide solid core doors fitted.
- Black powder coated slider windows windows fitted with security screens.
- Ceiling insulated with fiberglass bats (R1.5)
- House lined internally with 9mm CFC walls and 6mm CFC with plastic H joiners.
- Colour bond internal corner flashings fitted over CFC
- Ceiling fan in room
- LED downlights 4 of
- Electrical provisions provided for air conditioners.
- 2 double GPO's single outlets
- Black security screens
- Black security doors 920mm wide
- All doorways fitted with 920mm wide doors.
- Box air conditioning fitted to new bedroom.



Electrical Works

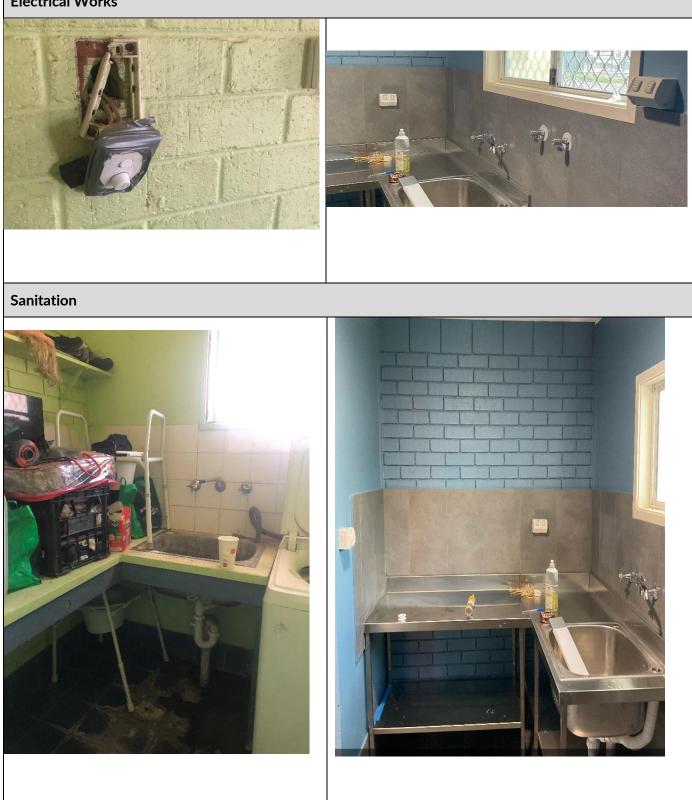

Visual Progress

Include before and after images of all areas that received upgrades. Delete/add areas as needed.



Completion Report

BEFORE

AFTER

Front Exterior



Left-Side Exterior






house 7 - *Rockhole Community*

Completion Report

Living Room



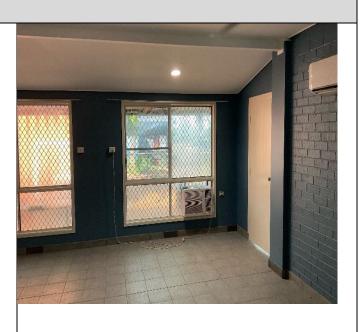


Kitchen






Bedroom 1

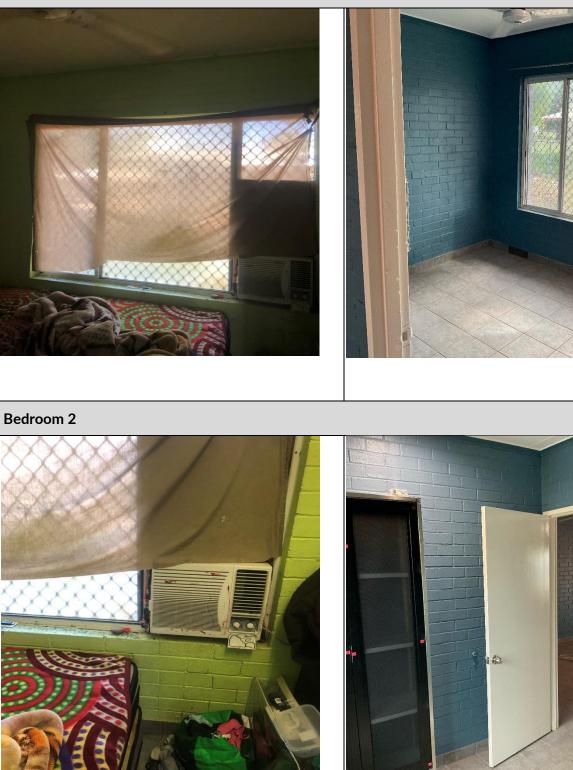

Department of Housing, Local Government and Community Development Version 1.0 – September 2024 Page 9 of 12




Bedroom 3 (New)

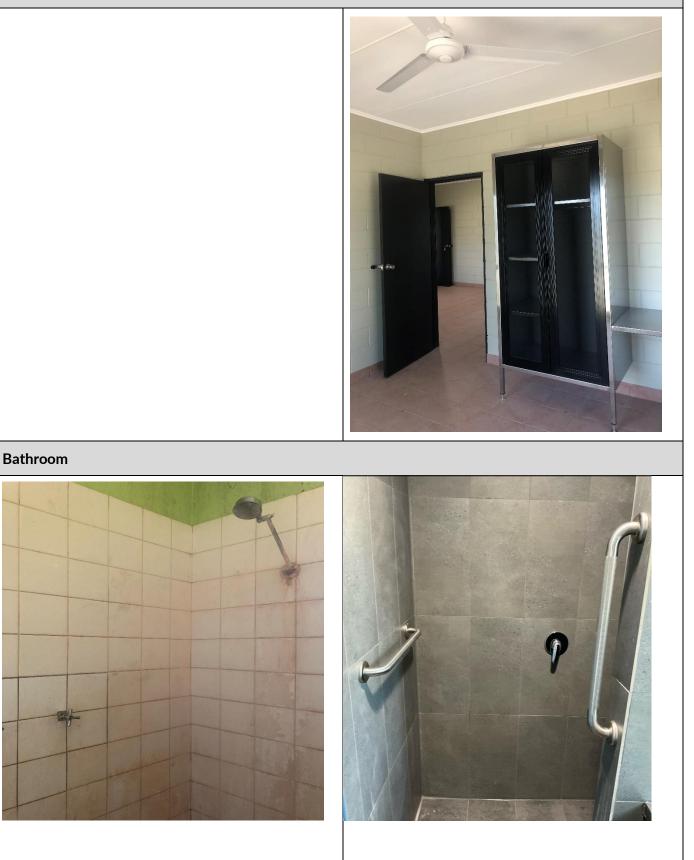

Department of Housing, Local Government and Community Development Version 1.0 – September 2024 Page 10 of 12



Toilet

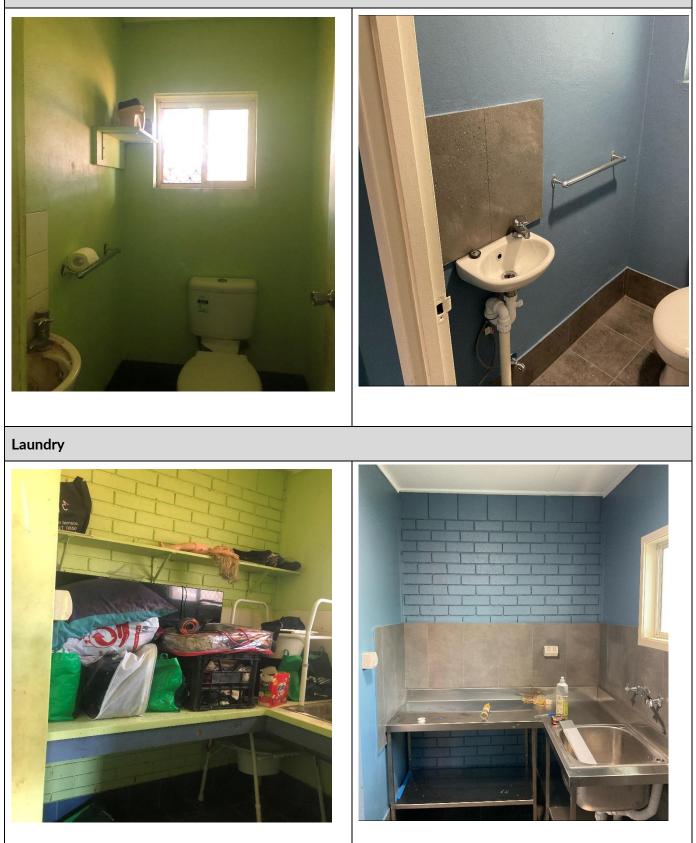

house 7 - *Rockhole Community*



Attachments

- ✓ Electrical Certificate of Compliance
- $\checkmark \quad {\sf Water Proofing Certification}$
- ✓ Glazing Certification
- ✓ Inspection Certificate
- ✓ Builders Declaration
