



## Completion Report FRM-144

Project Name:	HHIP2300001 Utopia – Clusters 2 & 4
Property Address:	House 14, Mosquito Bore Homeland.





## Table of Contents

1. Project Summary .....	3
2. Scope and Visual Confirmation of Works .....	4
2.1 Kitchen & Living Area .....	4
2.2 Bedrooms .....	5
2.3 Bathroom & Toilet Areas.....	6
2.4 Laundry & External Areas.....	7
3. Attachments .....	9
3.1 Electrical Certificate of Compliance.....	10
3.2 Waterproofing Certification .....	11
3.3 Glazing Certification.....	12

Service Provider	AEA NT PTY LTD PO Box 519 Katherine NT 0851
Contact numbers:	(08) 89722 211
Stephen Curry - Technical Services Manager	0427 215 952
Luke Wilks - Senior Project Manager	0476 156 419
John Binns - Project Manager (Central Region)	0427 650 058
Australian Business Number (ABN)	86 009 635 901
Contractor Accreditation Limited (CAL) Registration Number	K-28-10183-07-24
Asset No	House 14, Mosquito Bore Homeland.
Contract No.	HHIP2300001
Completion date	19/05/2024



## 1. Project Summary

House 14, Mosquito Bore Homeland.

The Homelands Housing and Infrastructure Program (HHIP), managed through the Department of Territory Families, Housing and Communities (TFHC) is a program funded by the Australian Government of which is focused on improving the living conditions in Homelands to ensure residents have access to safe, secure and quality housing and infrastructure suitable to their needs.

AEA NT have completed the approved scope of works at House 14, Mosquito Bore Homeland, delivering a quality final product which was handed back to the primary residents who now have improved access to the 9 Healthy Living Practices.

The construction works at House 14, Mosquito Bore Homeland commenced on 8<sup>th</sup> April 2024 and were completed on 19<sup>th</sup> of May 2024 representing a five (5) week works program.

The total labour hours expended on this project included 37% participation by Aboriginal staff and/or sub-contractors.

## 2. Scope and Visual Confirmation of Works

### 2.1 Kitchen & Living Area

- Install 2 x new solid core doors including entrance locksets (keyed alike with other external doors), door saver plates, weather seals, and door stops
- Install 1 x new solid core door with passage lockset to existing built-in pantry
- Install 3 x new windows (to suit existing openings), screens and flashings (1 x kitchen window and 1 x living area window without air-conditioning provision; 1 x living area window with box air-conditioner provision ONLY)
- Install curtain rod holders above 2 x living area windows only (holders only NO rods)
- Patch, prepare and paint all surfaces (walls, ceiling, door frames, doors, pantry shelves and window surrounds)
- Repair/replace damaged floor tiles including nosing tiles from external slab to weather strip under both external doors
- Supply and install new stainless steel kitchen benches
- Install new sink and flick mixer
- Remove small old nib wall and patch the floor and wall tiles
- Install new electrical components including stove and isolator, lights, light switches, ceiling fan, fan switch, power points (including new power point near window with A/C provision in living area), and smoke alarm.
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers
- Paint touchups

Before works commenced:



After works completed:



## 2.2 Bedrooms

### Bedroom 1

- Install 1 x new solid core door including privacy lockset and door stop
- Install 1 x new window, screen and flashings with box air-conditioner provision
- Install curtain rod holders above window (holders only NO rods)
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Repair/replace damaged floor tiles
- Clean, prepare and repaint existing steel framed mesh cupboard
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points (including new power point near window with A/C provision)
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers
- Paint touchups


### Bedroom 2

- Install 1 x new solid core door including privacy lockset and door stop
- Install 1 x new window, screen and flashings with box air-conditioner provision
- Install curtain rod holders above window (holders only NO rods)
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Repair/replace damaged floor tiles
- Clean, prepare and repaint existing steel framed mesh cupboard
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points (including new power point near window with A/C provision)
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers
- Paint touchups

### Bedroom 3

- Install 1 x new solid core door including privacy lockset and door stop
- Install 2 x new windows, screens and flashings (only 1 x window with box air-conditioner provision)
- Install curtain rod holders above window (holders only NO rods)
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Repair/replace damaged floor tiles
- Clean, prepare and repaint existing steel framed mesh cupboard
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points (including new power point near window with A/C provision)
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers
- Paint touchups

### Before Bedrooms works commenced:

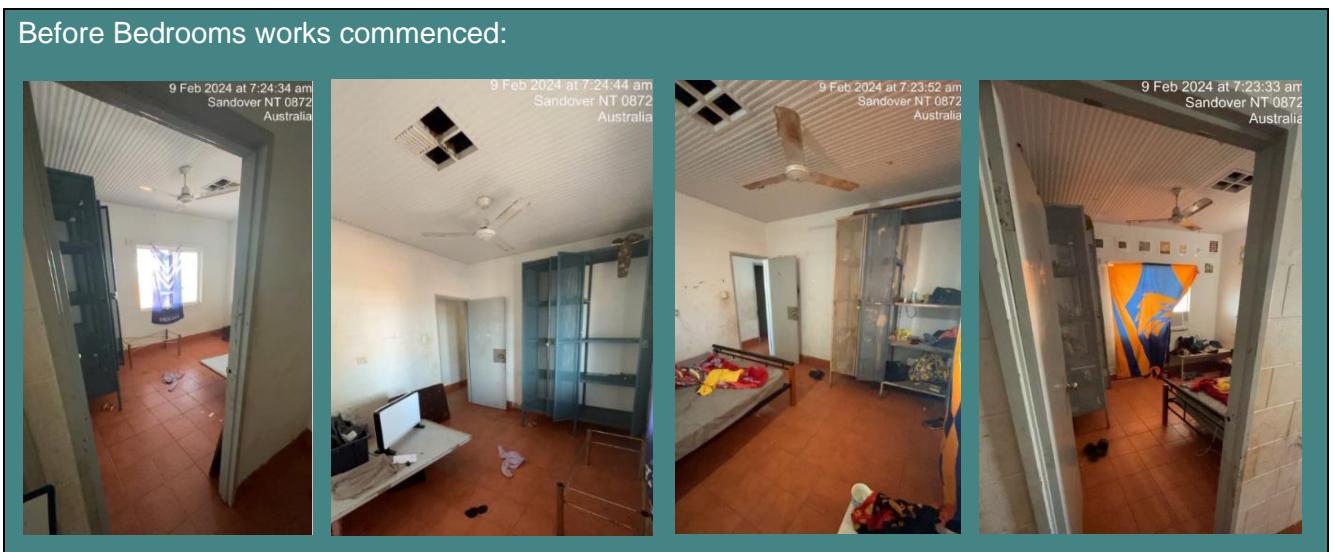



## After Bedrooms works completed:



## 2.3 Bathroom & Toilet Areas

### Bathroom

- Strip out bathroom including removing shower hob, wall and floor tiles
- Waterproof wet area walls and floor
- Prepare and lay screed bed with appropriate fall to floor waste
- Tile and grout floors, walls and skirting as required
- Install 1 x new solid core door including privacy lockset and door stop
- Install 1 x new vented window with screen and flashings
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Supply and install new plumbing fittings and fixtures including stainless steel shower mixer, outlet, shower rose, waste grate, stainless steel mixer & hand basin with splash back and mirror
- Supply and install new fixtures including towel rail, disabled grab rails, stainless steel soap holder, stainless steel shelves, and hooks to back of door
- Install new electrical components including light, switches, power points
- Paint touchups

### Toilet

- Install 1 x new solid core door including privacy lockset and door stop
- Install 1 x new vented window with screen and flashings (outside hood)
- Supply and install new plumbing fittings and fixtures including stainless steel mixer & hand basin with splash back, toilet pan, pan rubber, mini cistern cock and toilet roll holder
- Patch, prepare and paint all surfaces (walls, ceiling and new door)
- Repair/replace damaged floor tiles
- Install new electrical components – light and switch
- Paint touchups

## Before Bathroom & Toilet works commenced:



## After Bathroom & Toilet works completed:



## 2.4 Laundry & External Areas

### Laundry

- Install 1 x new solid core door including entrance lockset (keyed alike with other external doors), door saver plate, weather seal, and door stop
- Install 1 x new vented window with screen and flashings
- Patch, prepare and paint all surfaces (walls, ceiling and new door)
- Repair/replace damaged floor tiles including nosing tiles from external slab to weather strip under door
- Supply and install new laundry tub
- Service laundry taps
- Clean, prepare and repaint existing steel framed mesh cupboard
- Install new electrical components including light, switches, and power point
- Paint touchups

### Additional Toilet (Outside)

- Install 1 x new solid core door including entrance lockset (keyed alike with other external doors), door saver plate, weather seal, and door stop
- Install 1 x new vented window with screen and flashings
- Supply and install new plumbing fittings and fixtures including stainless steel mixer & hand basin with splash back, toilet pan, pan rubber, mini cistern cock and toilet roll holder
- Patch, prepare and paint all surfaces (walls, ceiling and new door)

- Repair/replace damaged floor tiles including nosing tiles from external slab to weather strip under door
- Install new electrical components – light and switch
- Paint touchups

## External Areas

- Service Solar Hot Water System
- Remove old unused/redundant chimney and patch roof and ceiling
- Prep and paint T-bar clothesline uprights and re-string with stainless steel line and tensioner
- Rear verandah (3000 x 6000) - pressure clean, prepare, fill cracks, Tuff Top and grind concrete slab
- Front verandah – supply and install new school type fencing similar to House 1 around the perimeter of slab with pedestrian access gate, including top and bottom rails, one additional post, hinges and gate with latch
- Pressure clean, prepare and paint external wall surfaces, posts and frames
- Provide 2 x concrete splash pads to suit existing outside garden taps
- Install new main water valve box with 600mm concrete surround
- Supply and install 6 x new yellow painted bollards around septic tank
- Install new electrical components including lights, switches, power points, meter isolator, RCDs, and compliant switchboard
- Service “swampy” air-conditioning unit (NOT split system)

## Before Laundry & External works commenced:



## After Laundry & External works commenced

