



## Completion Report FRM-144

Project Name:	HHIP2300001 Utopia – Clusters 2 & 4
Property Address:	House 8, Mosquito Bore Homeland.





## Table of Contents

1. Project Summary .....	3
2. Scope and Visual Confirmation of Works .....	4
2.1 Kitchen & Living Area .....	4
2.2 Bedrooms .....	5
2.3 Bathroom & Toilet Area .....	7
2.4 Laundry & External areas .....	8
3. Attachments .....	10
3.1 Electrical Certificate of Compliance .....	11
3.2 Waterproofing Certification .....	12
3.3 Glazing certificate .....	13
3.4 Talent Release Form .....	14

Service Provider	AEA NT PTY LTD PO Box 519 Katherine NT 0851
Contact numbers:	(08) 89722 211
Stephen Curry - Technical Services Manager	0427 215 952
Luke Wilks - Senior Project Manager	0476 156 419
John Binns - Project Manager (Central Region)	0427 650 058
Australian Business Number (ABN)	86 009 635 901
Contractor Accreditation Limited (CAL) Registration Number	K-28-10183-07-24
Asset No	House 8, Mosquito Bore Homeland.
Contract No.	HHIP2300001
Completion date	19/05/2024

## 1. Project Summary

House 8, Mosquito Bore Homeland.

The Homelands Housing and Infrastructure Program (HHIP), managed through the Department of Territory Families, Housing and Communities (TFHC) is a program funded by the Australian Government of which is focused on improving the living conditions in Homelands to ensure residents have access to safe, secure and quality housing and infrastructure suitable to their needs.

AEA NT have completed the approved scope of works at House 8, Mosquito Bore Homeland, delivering a quality final product which was handed back to the primary residents who now have improved access to the 9 Healthy Living Practices.

The construction works at House 8, Mosquito Bore Homeland commenced on 8<sup>th</sup> April 2024 and were completed on 19<sup>th</sup> of May 2023 representing a five (5) week works program.

The total labour hours expended on this project included 28% participation by Aboriginal staff and/or sub-contractors.



Picture of job completion handover with primary resident. Refer to 3.4 Talent Release Form

## 2. Scope and Visual Confirmation of Works

### 2.1 Kitchen & Living Area

- Install 2 x new door frames, solid core doors including entrance locksets (keyed alike with other external doors), door saver plates, weather seals, and door stops
- Install 2 x new windows, screens and flashings
- Install curtain rod holders above 1 x living area window only (holders only NO rods)
- Supply and install new RAC hatch provision in existing wall
- Install insulation batts in wall cavity
- Repair/service and pressure clean existing stainless-steel kitchen benches
- Install new kitchen sink bowl and flick mixer
- Install new stainless-steel splash back around kitchen bench area
- Supply and install new steel mesh pantry cupboard
- Patch, prepare and paint all surfaces (walls, ceiling, door frames, doors and window surrounds)
- Grind concrete floor ready for covering
- Prepare, tile and grout floor surfaces
- Install new electrical components including stove and isolator (relocate stove power supply and isolator to beside kitchen bench), lights, light switches, ceiling fan, fan switch, power points (including new power point near RAC hatch provision in living area), and smoke alarm.
- Paint touchups

Before works commenced:



After works completed:



## 2.2 Bedrooms

### Bedroom 1

- Install 1 x new door frame, solid core door including privacy lockset and door stop
- Install 1 x new window, screen and flashings
- Install curtain rod holders above window (holders only NO rods)
- Supply and install new RAC hatch provision in existing wall
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Grind concrete floor ready for covering
- Prepare, tile and grout floor surfaces
- Supply and install new steel mesh wardrobe
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points (including new power point near RAC hatch provision)
- Paint touchups

### Bedroom 2

- Install 1 x new door frame, solid core door including privacy lockset and door stop
- Install 1 x new window, screen and flashings
- Install curtain rod holders above window (holders only NO rods)
- Supply and install new RAC hatch provision in existing wall
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Grind concrete floor ready for covering
- Prepare, tile and grout floor surfaces
- Supply and install new steel mesh wardrobe
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points (including new power point near RAC hatch provision)
- Paint touchups



Before Bedrooms works commenced:



After Bedrooms works completed:



## 2.3 Bathroom & Toilet Area

- Remove existing separating wall and door frame to open area into combined shower/toilet
- Remove and replace sheet metal wall cladding in shower area
- Reline shower walls with 9mm villa board
- Waterproof wet areas walls and floor
- Prepare and lay screed bed with appropriate fall to floor waste
- Tile and grout floors, walls and skirting as required
- Install 1 x new door frame, solid core door including entrance lockset (keyed alike with other external doors), door saver plate, weather seal, and door stop
- Install new vented windows with screen and flashings (outside hood)
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Supply and install new plumbing fittings and fixtures including stainless steel shower mixer, outlet, shower rose, waste grate, stainless steel mixer & hand basin with splash back, toilet pan, pan rubber, mini cistern cock and toilet roll holder
- Supply and install new fixtures including towel rail, grab rails, stainless steel mirror above basin, stainless steel soap holder, stainless steel shelves and hooks to back of toilet door
- Install new electrical components including light, switches, power points
- Paint touchups

Before Bathroom & Toilet works commenced:



After Bathroom & Toilet works completed:



## 2.4 Laundry & External areas


### Laundry

- Construct 75mm stud wall clad with maxi-rib sheet metal at 3m long, to provide sheltered area for washing machine/laundry tub
- Prepare and paint all surfaces (walls and ceiling as required)
- Supply and install new plumbing fittings
- Supply and install new fixtures including laundry tub and splash back
- Install new electrical components including light, switch, and power point
- Construct new steel meshed enclosure to secure bathroom/laundry area, including: 50 x 50 SHS frame, 50 x 50 galvanised mesh fixed to frame, 900w x 2100h 50 x 50 gate with galvanised 50 x 50 mesh and entrance lockset (keyed alike with other external doors)
- Paint touchups

### External Areas

- Remove and replace electric HWS
- Install 2 x ramps at front and rear external access doorways
- Rear verandah - pressure clean concrete slab and concrete repairs with Tuff Top; construct full height wall, lined both sides, with 100mm gap between slab and bottom of new wall to eastern end of verandah
- Front verandah - form up and pour new concrete slab 12m x 3m; construct 900mm high nib wall with external sheet metal cladding, black slated sight screens above to approximately 1.8m high to eastern end only (3000 x 3000) to provide fit for purpose private outdoor area with suitable protection from the elements ("Wind Breaks")
- Pressure clean, prepare and paint external wall surfaces, posts and frames
- Relocate 2 x garden taps currently on front and rear verandahs to each end wall, and provide concrete splash pads to suit
- Install new main water valve box with 600mm concrete surround
- Supply and install 6 x new yellow painted bollards around septic tank
- Install new electrical components including lights, switches, power points, meter isolator, RCDs, and compliant switchboard
- Install new 1200 high chain-link perimeter fencing, 30m x 30m around house with 1 x double vehicular access gate and 2 x pedestrian access gates


Before Laundry & Exterior works commenced:

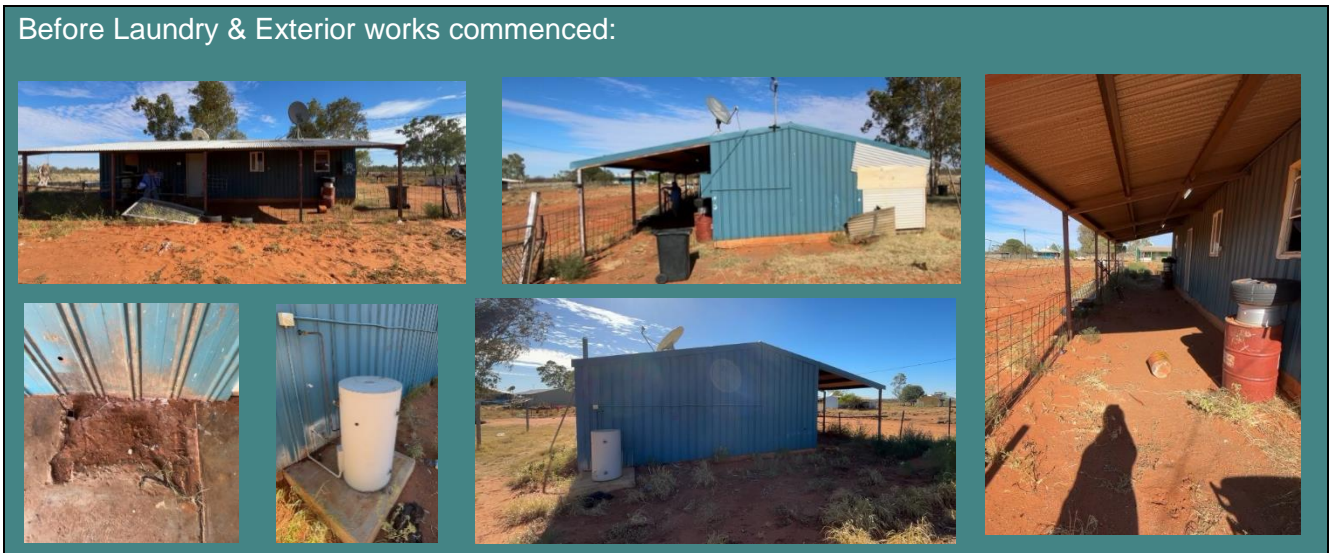





## After Laundry & Exterior works commenced

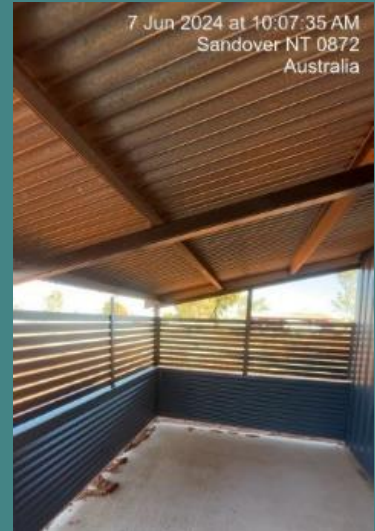



### 3. Attachments

- Electrical Certificate of Compliance
- Water Proofing Certification
- Glazing Certification
- Talent Release Form
