



Completion Report FRM-144

| | |
|-------------------|-------------------------------------|
| Project Name: | HHIP2300001 Utopia – Clusters 2 & 4 |
| Property Address: | House 3, Rocket Range Homeland. |





Table of Contents

| | |
|---|----|
| 1. Project Summary | 3 |
| 2. Scope and Visual Confirmation of Works | 4 |
| 2.1 Kitchen | 4 |
| 2.2 Bedrooms | 5 |
| 2.3 Bathroom & Toilet Area | 7 |
| 2.4 Laundry & Exterior areas. | 8 |
| 3. Attachments | 9 |
| 3.1 Talent Release form. | 10 |

| | |
|--|--|
| Service Provider | AEA NT PTY LTD PO Box 519 Katherine NT 0851 |
| Luke Wilks - Senior Project Manager | (08) 89722 211 |
| Australian Business Number (ABN) | 86 009 635 901 |
| Contractor Accreditation Limited (CAL) Registration Number | K-28-10183-07-24 |
| Asset No | House 3, Rocket Range Homeland. |
| Contract No. | HHIP2300001 |
| Completion date | 05/09/2024 |

1. Project Summary

House 3, Rocket Range Homeland.

The Homelands Housing and Infrastructure Program (HHIP), managed through the Department of Territory Families, Housing and Communities (TFHC) is a program funded by the Australian Government of which is focused on improving the living conditions in Homelands to ensure residents have access to safe, secure and quality housing and infrastructure suitable to their needs.

AEA NT have completed the approved scope of works at House 3, Rocket Range Homeland delivering a quality final product which was handed back to the primary residents who now have improved access to the 9 Healthy Living Practices.

The construction works at House 3, Rocket Range Homeland commenced 1st August and were completed on the 5th September 2024 representing a five (5) week works program.

The total labour hours expended on this project included 34% participation by Aboriginal staff and/or sub-contractors.



Picture of job completion handover with primary resident. Refer to *3.1 Talent Release Form*

2. Scope and Visual Confirmation of Works.

2.1 Kitchen

- Install new door frames, solid core doors including entrance locksets (keyed alike with other external doors), door saver plates, weather seals, and door stops
- Install new windows, screens and flashings
- Install curtain rod holders above window only (holders only NO rods)
- Supply and install new RAC hatch provision in existing wall
- Install insulation batts in wall/ceiling cavity where access permits
- Repair/service and pressure clean existing stainless-steel kitchen benches
- Install new flick mixer to existing sink
- Install new stainless-steel splash back around kitchen bench area
- Install new stainless-steel utensils draw to underside of existing kitchen bench
- Supply and install new double door steel mesh pantry cupboard
- Patch, prepare and paint all surfaces (walls, ceiling, door frames, doors and window surrounds)
- Grind concrete floor ready for covering
- Prepare, tile and grout floor surfaces
- Install new electrical components including stove, lights, light switches, ceiling fan, fan switch, power points (including new power point near RAC hatch provision in living area), and smoke alarm.

Before works commenced:



After works completed:





2.2 Bedrooms

Bedroom 1

- Install 1 x new door frame, solid core door including privacy lockset and door stop
- Install 1 x new window, screen and flashings
- Install curtain rod holders above window (holders only NO rods)
- Supply and install new RAC hatch provision in existing wall
- Install insulation batts in wall/ceiling cavity where access permits
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Grind concrete floor ready for covering
- Prepare, tile and grout floor surfaces
- Clean, service and repaint existing single door steel mesh wardrobe
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points (including new power point near RAC hatch provision)
- Paint touchups

Bedroom 2

- Install 1 x new door frame, solid core door including privacy lockset and door stop
- Install 1 x new window, screen and flashings
- Install curtain rod holders above window (holders only NO rods)
- Supply and install new RAC hatch provision in existing wall
- Install insulation batts in wall/ceiling cavity where access permits
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Grind concrete floor ready for covering
- Prepare, tile and grout floor surfaces
- Supply and install new single door steel mesh wardrobe
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points (including new power point near RAC hatch provision)
- Paint touchups

Bedroom 3 - Additional room (Rear Verandah)

- Prep existing verandah concrete slab and pour 3000 x 3600 x 100mm concrete topper to tie into house slab height
- Install new 75mm top-hat ceiling battens to existing roof structure
- Install new 75mm stud walls and clad external lining with maxi-rib metal sheeting
- Install wall and ceiling insulation and clad internal linings with maxi-rib metal sheeting
- Install 1 x new window, screen and flashings
- Install curtain rod holders above window (holders only NO rods)
- Install 1 x new door frame, solid core door including entrance lockset (keyed alike with other external doors), door saver plate, weather seal, and door stop
- Install new RAC hatch provision in existing wall
- Install flashings to suit and make vermin proof
- Prepare, tile and grout floor surfaces
- Supply and install new single door steel wardrobe
- Install new electrical components including light, light switch, fan, fan switch, power points (including power point near RAC hatch provision)
- Paint door frame and door and any other required touchups

Before Bedrooms works commenced:



After Bedrooms works completed:




2.3 Bathroom & Toilet Area.

Bathroom & Toilet Area

- Remove shower tray/bath and remove sheet metal wall cladding in shower area
- Reline shower walls with 9mm villa board
- Waterproof wet area walls and floor
- Prepare and lay screed bed with appropriate fall to floor waste
- Tile and grout floors, walls as required
- Install 1 x new door frame, solid core door including entrance lockset (keyed alike with other external doors), door saver plate, weather seal, and door stop
- Install 1 x new vented window with screen and flashings (outside hood)
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Supply and install new plumbing fittings and fixtures including stainless steel shower mixer, outlet, shower rose, waste grate, stainless steel mixer & hand basin with splash back, toilet pan, pan rubber, mini cistern cock and toilet roll holder
- Supply and install new fixtures including towel rails, grab rails, stainless steel mirror above basin, stainless steel soap holder, stainless steel shelves and hooks to back of door
- Install new electrical components including light, switches, power points
- Paint touchups

Before Bathroom & Toilet works commenced:

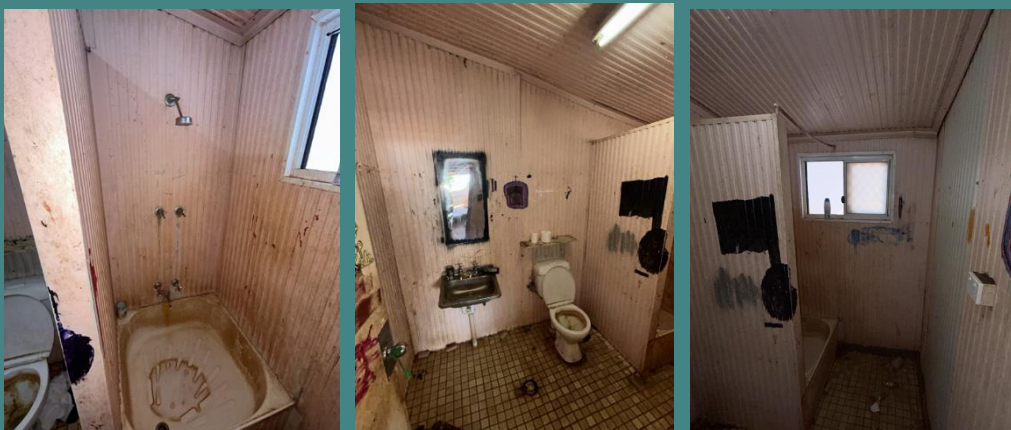

After Bathroom & Toilet works commenced:



2.4 Laundry & Exterior areas.

Laundry (Outside)

- Extend outside nib wall to provide added protection for washing machine/laundry tub area
- Prepare and paint all surfaces (walls, posts and ceiling as required)
- Supply and install new plumbing fittings including water pipes, drain pipes and 1/4 turn taps
- Supply and install new fixtures including laundry tub, stainless steel splash back and stainless steel shelf
- Install new electrical components including light, switch, and power point
- Paint touchups

External Areas

- Remove electric HWS and replace with 80L unit
- Install ramps at front and rear access doorways, as well as bathroom access door
- Prep and paint existing T-bar clothesline uprights and re-string with stainless steel line and tensioners
- Rear verandah - Construct new steel meshed enclosure to secure rear verandah area (new bedroom 3 and bathroom/laundry area), including: 50 x 50 SHS frame, 50 x 50 galvanised mesh fixed to frame, standard *Barker Humes* door with entrance lockset (keyed alike with other external doors)
- Front verandah - Construct 3000 x 3000 x 75mm steel stud frame 800mm high with 100mm gap from existing concrete slab with external custom-orb cladding and flashings (to be painted to match external house colour). Above stud frame, black aluminium slats to be installed to create sight screens above to approximately 1.8m high providing fit for purpose private outdoor areas with suitable protection from the elements ("Wind Breaks").
- Pressure clean, prepare and paint external wall surfaces, posts and frames
- Relocate garden taps currently on front and rear verandahs to each end wall, and provide concrete splash pads to suit
- Install new main water valve box with 600mm concrete surround
- Supply and install new yellow painted bollards around septic tank, 500mm in the ground with 900mm above ground to provide visual markers and also restrict vehicular access across buried infrastructure
- Install new electrical components including lights, switches, power points, meter isolator, RCDs, and compliant switchboard

Before Laundry & Exterior works commenced:



After Laundry & Exterior works



3. Attachments

- Glazing Certification
- Talent Release Form
