



Completion Report FRM-144

Project Name:	HHIPC00002 Petyale, Ileparratye & Adelaide Bore
Property Address:	House 1 – Ileparratye Homeland





Table of Contents

1. Project Summary	3
2. Scope and Visual Confirmation of Works	4
2.1 Kitchen & Living.....	4
2.2 Bedrooms	6
2.3 Combined Bathroom, Toilet and Laundry Area	8
2.3 External Areas.....	10
3. Attachments	11

Service Provider	AEA NT PTY LTD PO Box 519 Katherine NT 0851
Contact numbers: Luke Wilks - Operations Manager	(08) 89722 211 0476 156 419
Australian Business Number (ABN)	86 009 635 901
Contractor Accreditation Limited (CAL) Registration Number	K-28-10183-07-24
Asset No	House 1, Ileparratye Homeland
Contract No.	HHIPC00002
Completion date	24/02/2025



1. Project Summary

House 1 – Ilepparratye Homeland

The Homelands Housing and Infrastructure Program (HHIP), managed through the Department of Territory Families, Housing and Communities (TFHC) is a program funded by the Australian Government of which is focused on improving the living conditions in Homelands to ensure residents have access to safe, secure and quality housing and infrastructure suitable to their needs.

AEA NT have completed the approved scope of works at House 1, Ilepparratye Homeland delivering a quality final product which was handed back to the primary residents who now have improved access to the 9 Healthy Living Practices.

The construction works at House 1, Ilepparratye Homeland commenced on 6th of January and were completed on 24th of February 2025 representing a seven (7) week works program.

The total labour hours expended on this project included 37.5% participation by Aboriginal staff and/or sub-contractors.



2. Scope and Visual Confirmation of Works

2.1 Kitchen & Living


Kitchen

- Service existing glass sliding door (lockset to be keyed alike with other external doors).
- Supply and install 1 x diamond grill sliding security screen door.
- Supply and install new double door steel mesh pantry cupboard.
- Service 2 x windows.
- Supply and install 2 x diamond grill security screens to windows.
- Install curtain rod holders above windows (holders only NO rods).
- Patch, prepare and paint all surfaces (walls, ceiling, door frames, doors, and window surrounds).
- Grind concrete floor ready for covering.
- Prepare, tile and grout floor surfaces.
- Supply and install new stainless steel kitchen benches with stainless steel splash back.
- Install new double bowl sink and flick mixer.
- Install new electrical components including stove and isolator, lights, light switches, ceiling fan, fan switch, power points and smoke alarm.
- Paint touch-ups.

Living Area

- Install 1 x new solid core door including entrance locksets (keyed alike with other external doors), door saver plate, weather seal, and door stop.
- Service 1 x windows.
- Supply and install 1 x diamond grill security screens to window.
- Install curtain rod holders above window (holders only NO rods.)
- Patch, prepare and paint all surfaces (walls, ceiling, door frames, doors, and window surrounds)
- Grind concrete floor ready for covering.
- Prepare, tile and grout floor surfaces.
- Clad over existing ceiling with maxi-rib sheeting and flashings.
Install new electrical components including lights, light switches, ceiling fan, fan switch, power points and smoke alarm.
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers.
- Paint touch-ups.

Before works commenced:

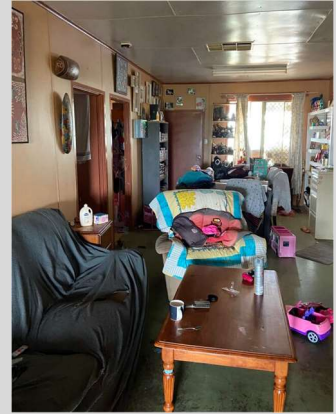

After works completed:





2.2 Bedrooms

Bedroom 1

- Install 1 x new solid core door including privacy lockset and door stop.
- Service window.
- Supply and install 1 x diamond grill security screens to window.
- Install curtain rod holders above window (holders only NO rods).
- Clad over existing ceiling with maxi-rib sheeting and flashings.
- Clean, patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Grind concrete floor ready for covering.
- Prepare, tile and grout floor surfaces.
- Supply and install new 3-door robe.
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points.
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers.
- Paint touch-ups.

Bedroom 2

- Install 1 x new solid core door including privacy lockset and door stop.
- Service window.
- Supply and install 1 x diamond grill security screens to window.
- Install curtain rod holders above window (holders only NO rods).
- Clad over existing ceiling with maxi-rib sheeting and flashings.
- Clean, patch, prepare and paint all surfaces (walls, ceiling, door and window frames).
- Grind concrete floor ready for covering.
- Prepare, tile and grout floor surfaces.
- Supply and install new 3-door robe.
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points.
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers.
- Paint touch-ups.

Bedroom 3

- Install 1 x new solid core door including privacy lockset and door stop.
- Service window.
- Supply and install 1 x diamond grill security screens to window.
- Install curtain rod holders above window (holders only NO rods).
- Clad over existing ceiling with maxi-rib sheeting and flashings.
- Clean, patch, prepare and paint all surfaces (walls, ceiling, door and window frames).
- Grind concrete floor ready for covering.
- Prepare, tile and grout floor surfaces.
- Supply and install new 3-door robe.
- Install new electrical components including light, light switch, ceiling fan, fan switch, power points.
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers.
- Paint touch-ups.

Bedroom 4

- Install 1 x new solid core door including privacy lockset and door stop.
- Service window.
- Supply and install 1 x diamond grill security screens to window.
- Install curtain rod holders above window (holders only NO rods).
- Clad over existing ceiling with maxi-rib sheeting and flashings.
- Clean, patch, prepare and paint all surfaces (walls, ceiling, door and window frames).
- Grind concrete floor ready for covering.
- Prepare, tile and grout floor surfaces.
- Supply and install new 3-door robe.

- Install new electrical components including light, light switch, ceiling fan, fan switch, power points.
- Replace existing ceiling air-conditioning vents with PVC grid mesh covers.
- Paint touch-ups.

Before Bedrooms works commenced:



After Bedrooms works completed:






2.3 Combined Bathroom, Toilet and Laundry Area

- Strip out room including removing shower screen, toilet suite, vanity, laundry tub, 'shower' window, shower wall lining, tiles throughout and all fittings and fixtures.
- Frame up new window opening and install 1 x new vented window with screen and flashings (outside hood).
- Construct 2 x new nib walls for shower recess allowing appropriate width for adjacent accessible toilet access.
- Line shower walls with 9mm villa board.
- Waterproof shower/wet area walls and floor.
- Prepare and lay screed bed in shower area with appropriate fall to floor waste.
- Tile and grout floors and walls of shower area, and floor and skirting through remainder of room.
- Clad over existing ceiling with maxi-rib sheeting and flashings.
- Install 1 x new solid core door including entrance lockset (keyed alike with other external doors), door saver plate, weather seal, and door stop.
- Install 1 x new solid core door including privacy lockset and door stop.
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames).
- Supply and install new plumbing fittings and fixtures including stainless steel shower mixer, outlet, shower rose, waste grate, stainless steel mixer, vanity unit with tile splash back, toilet pan, pan rubber, mini cistern cock and toilet roll holder.
- Supply and install new fixtures including 2 x towel rail, 2 x grab rails (1 x toilet; 1 x shower), stainless steel soap holder.
- Supply and install new double door steel framed mesh cupboard.
- Service 2 x louvred windows (toilet and laundry).
- Service existing laundry taps.
- Supply and install new laundry tub with tile splash back.
- Install new electrical components including light, switches, power points.
- Paint touch-ups .

Before Bathroom & Toilet works commenced:

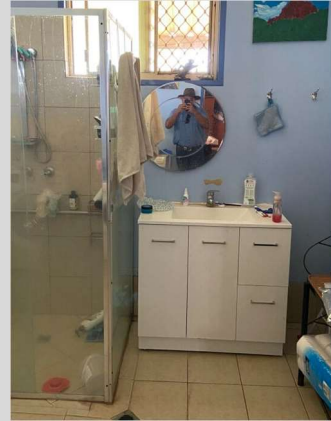

After Bathroom & Toilet works completed:



2.3 External Areas.

External Areas

- Service Solar Hot Water System.
- Replace old gas regulator with new pigtail gas line to bottle.
- Rear verandah - pressure clean.
- Front verandah – pressure clean.
- Pressure clean, prepare and paint external wall surfaces, posts and frames.
- Install 1 x tamper proof cage for existing pressure pump.
- Supply and install 6 x new yellow painted bollards around septic tank.
- Form up and pour 2 x concrete slabs (3m wide x 17m long) on both right and left hand side of house to reduce dust and provide hard stand under existing roof line.
- Install new electrical components including lights, switches, power points, meter isolator, RCDs, and compliant switchboard.
- Service “swampy” air-conditioning unit (NOT split system).

Before Laundry & Exterior works commenced:



After Laundry & Exterior works completed:





3. Attachments

Electrical Safety Certificate of Compliance

Waterproofing Certification
