



## Completion Report FRM-144

Project Name:	HHIP2300001 Utopia – Clusters 2 & 4
Property Address:	House 60 – Arlparra Homeland





## Table of Contents

1. Project Summary .....	3
2. Scope of Works .....	4
2.1 Kitchen (New Build Room) .....	4
2.2 Bedrooms .....	4
2.3 Bathroom & Toilet Works .....	5
2.3 Laundry & Exterior Areas .....	5
3. Visual Progress .....	7
4. Attachments .....	10

<b>Service Provider</b>	AEA NT PTY LTD	<b>ABN</b>	86 009 635 901
<b>Contact Details</b>	Tawhai Carter Deputy CEO E. tawhai@aeagp.com.au	<b>Contractor Accreditation Limited (CAL) Registration Number</b>	K-28-10183-07-24
<b>Project Name</b>	Utopia Clusters 2 & 4	<b>Contract No.</b>	HHIP2300001
<b>Homeland</b>	Arlparra	<b>Community ID</b>	168
<b>Project Type</b>	House & Infrastructure Upgrade	<b>House #</b>	60
<b>Commencement Date</b>	16/06/2025	<b>Completion Date</b>	18/09/2025

## 1. Project Summary


House 60, Arlparra Homeland

The Homelands Housing and Infrastructure Program (HHIP), managed through the Department of Territory Families, Housing and Communities (TFHC) is a program funded by the Australian Government of which is focused on improving the living conditions in Homelands to ensure residents have access to safe, secure and quality housing and infrastructure suitable to their needs.

AEA NT have completed the approved scope of works at House 60, Arlparra Homeland delivering a quality final product which was handed back to the primary residents who now have improved access to the 9 Healthy Living Practices.

The construction works at House 60, Arlparra Homeland commenced on the 16<sup>th</sup> of June 2025 and were completed on the 18<sup>th</sup> of September 2025, representing a fourteen (14) week works program.

The total labour hours expended on this project included 35% participation by Aboriginal staff and/or sub-contractors.

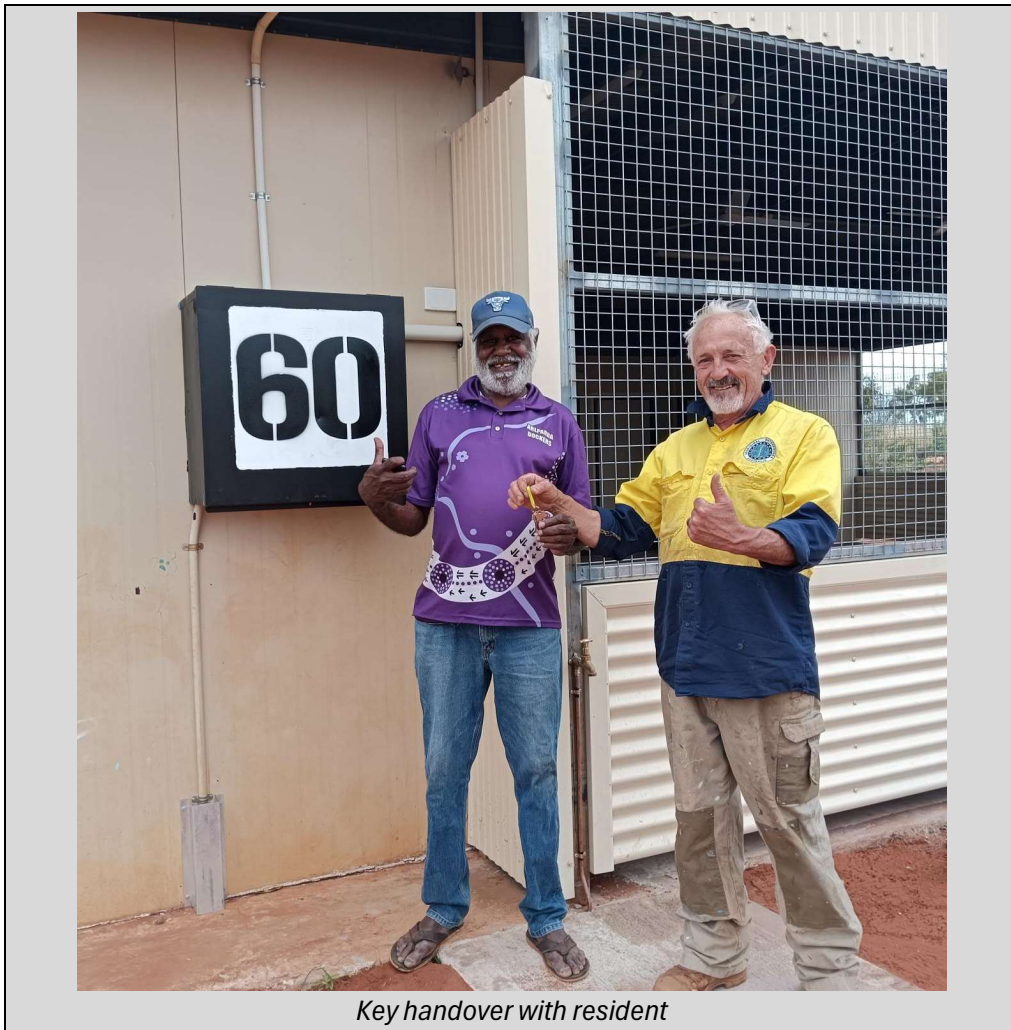

*Key handover with resident*



## 2. Scope of Works

### 2.1 Kitchen (New Build Room)

- Provide new enclosed kitchen (2500x4500) with 75mm insulated wall panels.
- Install 1 x new 920 door frame, solid core doors including entrance locksets (keyed alike with other external doors), door saver plates, weather seals, and door stops
- Install 1 x new window, screens and flashings
- Supply and install new exhaust fan
- Supply and install new wall mount fan
- Repair/service and pressure clean existing stainless-steel kitchen benches
- Install new flick mixer to existing sink
- Install new stainless-steel splash back around kitchen bench area
- Install new stainless-steel utensils draw to underside of existing kitchen bench
- Supply and install new double door steel mesh pantry
- Patch, prepare and paint all surfaces (walls, ceiling, door frames, doors and window surrounds)
- Grind concrete floor ready for covering
- Prepare, tile and grout floor surfaces
- Install new electrical components including stove and isolator (New stove power supply and isolator to beside kitchen bench), lights, light switches, power points and smoke alarm.

### 2.2 Bedrooms

#### Bedroom 1 (Left)

- Cut into existing wall and Install 1 x new door frame, solid core door including privacy lockset and door stop
- Delete existing door from passage to bedroom 1 and infill with insulated wall panel
- Supply & install new security door (keyed alike with other external doors).
- Service only 1 x window, screen and flashings
- Install curtain rod holders above window (holders only NO rods)
- Patch, prepare and paint all surfaces internal only (walls, ceiling, door and window frames)
- Clean existing floor covering and apply a clear coat sealer
- Clean existing single door steel mesh wardrobe
- Install new electrical components including light, light switch, wall mounted fan, fan switch, power points
- Paint touchups

#### Bedroom 2 (Middle)

- Remove existing internal bedroom/passageway wall.
- Remove existing sliding door from external wall.
- Install 1 x new door frame, solid core door including privacy lockset and door stop.
- Supply & install new security door (keyed alike with other external doors).
- Service 1 x window, screen and flashings
- Install curtain rod holders above window (holders only NO rods)
- Patch, prepare and paint all surfaces internal only (walls, ceiling, door and window frames)
- Clean existing floor covering and apply a clear coat sealer
- Clean existing single door steel mesh wardrobe
- Install new electrical components including light, light switch, Wall mounted fan, power points
- Paint touchups



## Bedroom 3 (Right)

- Delete existing door from passage to bedroom 3 and infill with insulated wall panel.
- Supply & install new security door (keyed alike with other external doors).
- Service only 1 x window, screen and flashings
- Install curtain rod holders above window (holders only NO rods)
- Patch, prepare and paint all surfaces internal only (walls, ceiling, door and window frames)
- Clean existing floor covering and apply a clear coat sealer
- Clean existing single door steel mesh wardrobe
- Install new electrical components including light, light switch, wall mounted fan, fan switch, power points
- Paint touchups

## 2.3 Bathroom & Toilet Works

### Bathroom & Toilet Area

- Remove existing Vinyl flooring
- Supply and install new insulated wall dividing shower and toilet area x 1200 in length
- Prepare and lay screed bed with appropriate fall to floor waste
- Tile and grout floors as required
- Supply and install new exhaust fan
- Supply and install new laminated wall panels to shower cubical area
- Supply and install new plumbing fittings and fixtures including stainless steel shower mixer, outlet, shower rose, waste grate, stainless steel mixer, splash back, toilet pan, pan rubber, mini cistern cock and toilet roll holder
- Supply and install new fixtures including 1 x towel rail, grab rails, 1 x stainless steel mirror above existing basin, stainless steel soap holder, 3 x stainless steel shelves and 4 x hooks to back of door.
- Patch, prepare and paint all surfaces (walls, ceiling, door and window frames)
- Install 1 x new 920 solid core door including Privacy lock set, door saver plate, weather seal, and door stop
- Service x 1 window with screen and flashings.
- Install new electrical components including light, switches, power points
- Paint touchups

## 2.3 Laundry & Exterior Areas

### Laundry (Inside)

- Clean and seal existing Vinyl flooring
- Install 1 x new door frame, solid core door including privacy lockset, door saver plate, weather seal, and door stop
- Supply and install new plumbing fittings, drainpipes and 1/4 turn taps
- Supply and install new laundry trough, mixer and stainless steel splashback
- Prepare and paint all surfaces (walls and ceiling as required)
- Service x 1 vented window with screen and flashings.
- Install new electrical components including light, switch, exhaust fan and power point
- Paint touchups.



## External Areas

- Remove existing electric HWS and replace with 120lt
- Prep and paint existing T-bar clothesline uprights and re-string with stainless steel line and tensioners
- Supply and install new 90x90 shs galvanized corner support post x1
- Pressure clean all concrete external surfaces
- Construct a steel frame along front and sides of outdoors area and sheet with external custom-orb cladding and flashings to the height off 800mm with a 100mm gap from existing concrete slab. (paint to match existing external house colour). Construct above the custom-orb 50 x 50 mesh to allow for breeze to entre the area and above the mesh sheet construct steel frame with external custom-orb cladding to create a fully secure enclosure space to the full length and height of the front and sides. Include 2 x standard *Barker Humes* doors with entrance lockset (keyed alike with other external doors)
- Relocate 1 x garden taps currently on front and relocate to the outer edge of concrete and provide concrete splash pads to suit.
- Supply and install 6 x new yellow painted bollards around septic tank and IO risers, 500mm in the ground with 900mm above ground to provide visual markers and also restrict vehicular access across buried infrastructure
- Install new electrical components including 3 x lights, switches, power points and 3 x ceiling fans (600mm drop), meter isolator, RCDs.

## 3. Visual Progress

**Before**



**After**



**Before**



**After**





**Before**



**After**



**Before**



**After**



**Before**



**After**



**Before**



**After**



## Before



## After



## 4. Attachments

- Talent Release Form
- Electrical Certificate of Compliance
- Waterproofing Certification
